

WISCONSIN RAPIDS PUBLIC WORKS DIVISION
PUBLIC WORKS PROJECT UPDATES
April 5th, 2024 Update #1

City Engineer:

Joe Eichsteadt, PE
Phone (715) 421-8251
Jeichsteadt@wirapids.org

Assistant City Engineer:

Nick Dums, PE
Phone (715) 421-8209
Ndums@wirapids.org

Public Works Superintendent

Paul Vollert
Phone (715) 421-8218
Pvollert@wirapids.org



Lincoln Street at Chestnut Street

○ **Lincoln Street (Expressway to E Grand Ave)**

Current Phase: Phase 1 – underground utility replacement will take approximately 2 weeks.


Current Closure: Intersection at Chestnut St and north along Lincoln St to Witter Street. D Street is still accessible to residents.

This Week


- Work began at the intersection of Chestnut St and Lincoln St on Monday, April 1st with the removal of pavement.
- On Tuesday additional pavement was removed to Witter St.
- No work occurred on Wednesday due to the snow event.
- On Thursday & Friday, the water main was capped in the intersection and preparations are being made for excavating sanitary and storm sewer next week.

Next Week

- Storm sewer and sanitary sewer utility replacement will continue within the intersection of Chestnut St and Lincoln St.

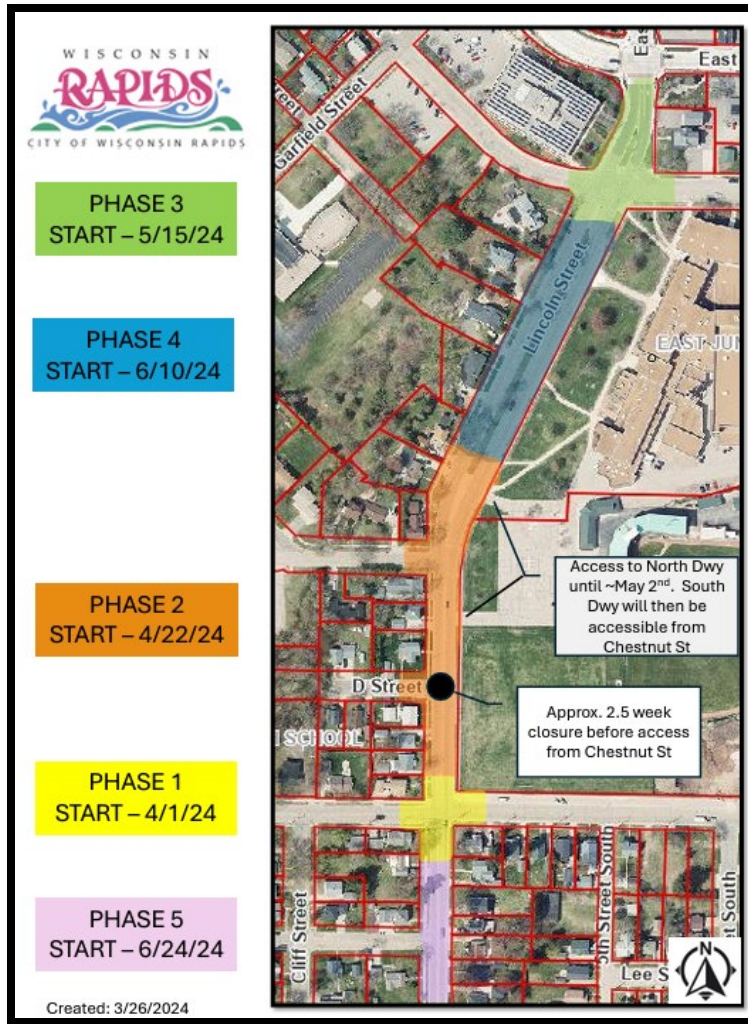

- **Sidewalk Maintenance**
Sidewalk maintenance work began on 3/25/24. The sidewalk work is primarily occurring between 12th St S, Plover Rd, Daly St, and E Grand Ave. The Contractor plans to begin pouring concrete next week.

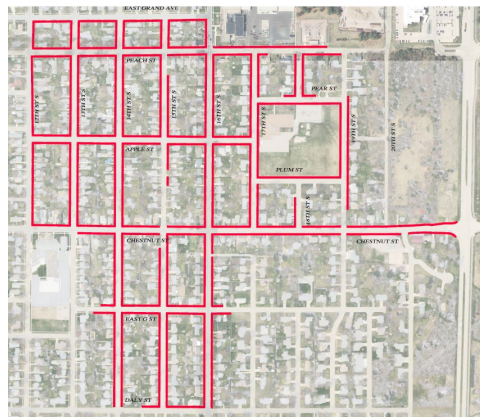

For more information please follow these links

Project Information, plans, schedule, street closure notifications - <https://www.wirapids.org/construction-projects.html>

Project Updates and Road Closure Notifications can be subscribe to at <https://www.wirapids.org/construction-projects.html>
5-year Public Works Capital Improvement Plan can be accessed at www.wirapids.org/engineering
