

WISCONSIN RAPIDS PUBLIC WORKS DIVISION
PUBLIC WORKS PROJECT UPDATES
April 12th, 2024 Update #2

City Engineer:


Joe Eichsteadt, PE
Phone (715) 421-8251
Jeichsteadt@wirapids.org

Assistant City Engineer:

Nick Dums, PE
Phone (715) 421-8209
Ndums@wirapids.org

Public Works Superintendent

Paul Vollert
Phone (715) 421-8218
Pvollert@wirapids.org

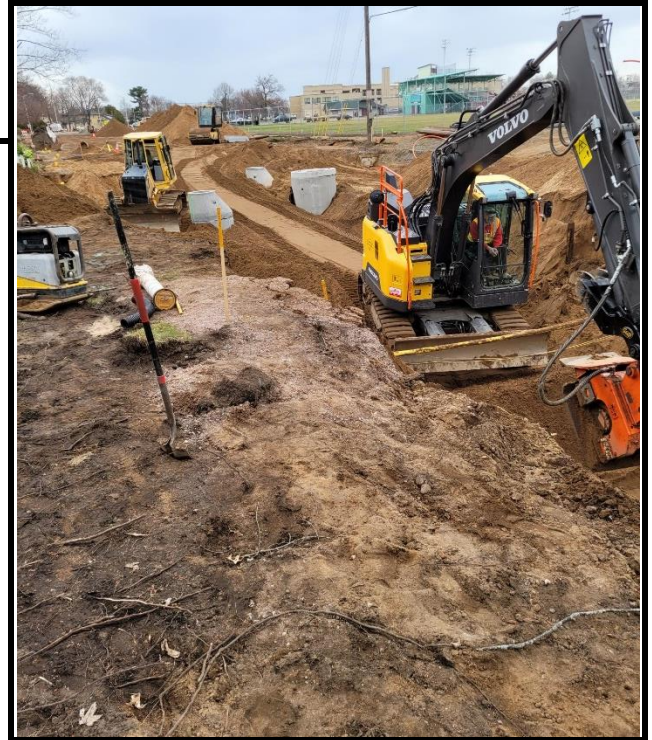

Lincoln Street at Chestnut Street

○ **Lincoln Street (Expressway to E Grand Ave)**

Current Phase: Phase 1 – underground utility replacement will take approximately 2 weeks.
Current Closure: Intersection at Chestnut St and north along Lincoln St to Witter Street. D Street is still accessible to residents.

This Week

- Sanitary sewer replacements occurred within the intersection of Chestnut St and Lincoln St.

Next Week

- Water main and storm sewer work will continue within the intersection of Chestnut St and Lincoln St. Utilities are expected to be replaced up to 'D' Street by the end of next week.

Project Phasing Map


https://www.wirapids.org/uploads/1/0/3/3/103347874/construction_schedule_03262024.pdf

○ **Sidewalk Maintenance**

Next week the contractor plans to pour sidewalk on 14th, 15th, 16th streets south of Chestnut St.

○ **Curb Maintenance**

Next week the contractor plans to pour curb within the sidewalk maintenance area north of Chestnut St

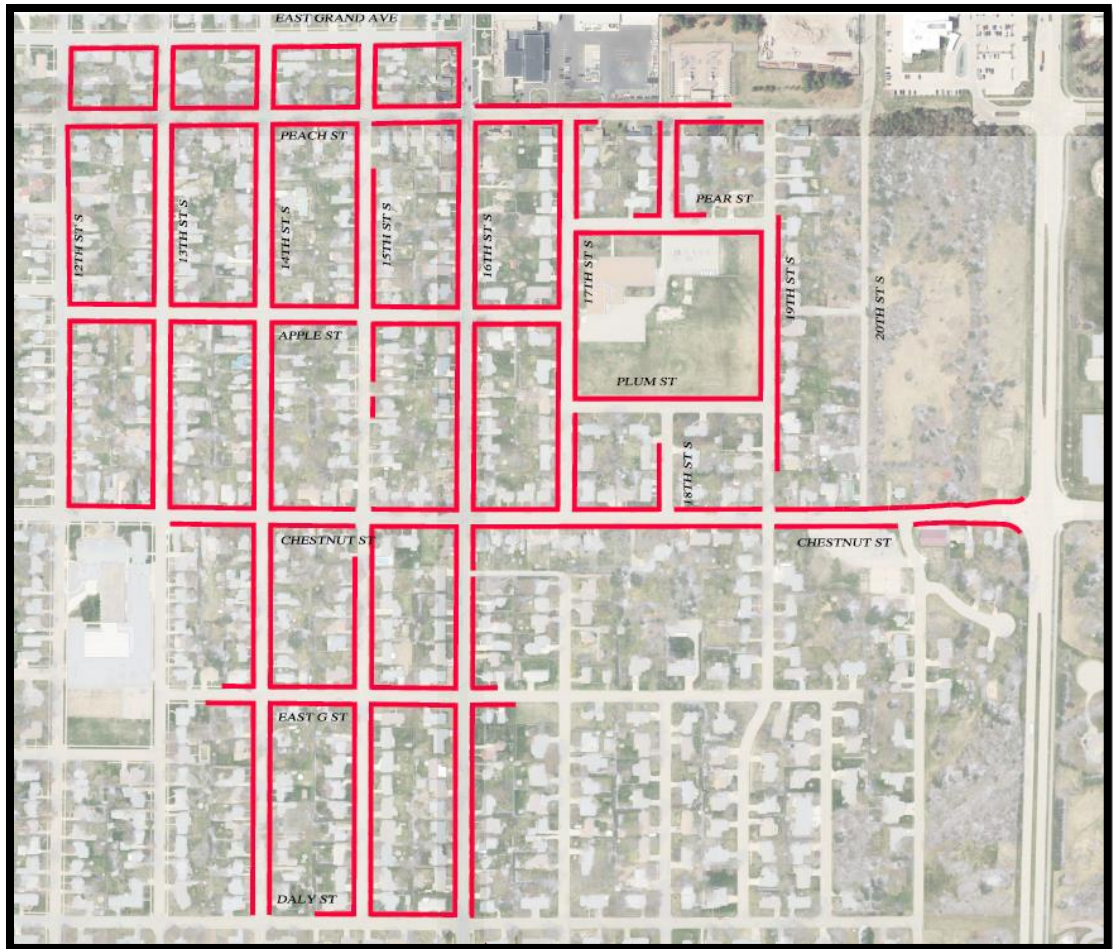

2024 Sidewalk Maintenance Area

For more information please follow these links

Project Information, plans, schedule, street closure notifications - <https://www.wirapids.org/construction-projects.html>

Project Updates and Road Closure Notifications can be subscribe to at <https://www.wirapids.org/construction-projects.html>
5-year Public Works Capital Improvement Plan can be accessed at www.wirapids.org/engineering
