


WISCONSIN RAPIDS PUBLIC WORKS DIVISION
PUBLIC WORKS PROJECT UPDATES
Sept. 10th, 2021 Update #18

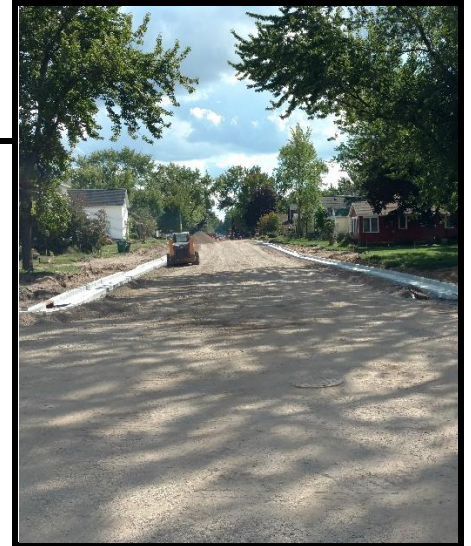

18th Ave curb and gutter

Director of Public Works: Joseph Terry
Phone (715)-421-8255
Email JTerry@wirapids.org

City Engineer: Joe Eichsteadt
Phone (715)-421-8251
Email Jeichsteadt@wirapids.org

- **8th St Culvert Rehabilitation**
 - Project is complete except for parking lot patching adjacent to the road.
 - Asphalt patching is scheduled for next Tuesday, 9/14.

- **18th Ave S – Russell St to W Grand Ave**
 - *Essex St to W Grand Ave – curb & gutter work began on Wednesday, September 8th and was complete on Thursday, September 9th. Sidewalk and driveways is anticipated to begin in the next two weeks.*
 - Sanitary sewer installation between Chase St and Essex was completed on Thursday of this week.
 - Crews replaced water main this week between Chase St and Essex and began replacement of sanitary laterals.
 - Work next week will include completion of the sanitary laterals and crews will begin work on the storm sewer.

- **11th St N – Washington St to Apricot St**
 - Hydro-seeding is scheduled for next week.

- **1st St N – Near Love St**
 - This project is a being performed by We Energies as part of infrastructure enhancements for local industries. The anticipated completion date is 10/08/2021. If you have specific questions or concerns about this project please contact Tom Krostag, Sr. Operations Supervisor – Major Projects at WE Energies. 715-421-7268, Thomas.krostag@we-energies.com

- **Rapids East Commerce Center Rail Extension**
 - Advertising for bids begins Saturday, September 4th. Construction work is anticipated this fall.

- **Sidewalk Maintenance**
 - *Sidewalk maintenance work will continue during the month of September*

- **Grove Ave Utility Extension (Quadplex Project)**
 - Main line utilities will be installed on Grove Ave from 21st PI S approximately 500' west. Work is scheduled for late fall.

- **Completed Projects**
 - 15th St N (Apricot St to Norton St), Jefferson St (25th Ave N to east terminus), Joint Sealing on Plover Road from Washington St to City Limits, Chip Sealing, Curb Maintenance

For more information please follow these links

Construction Schedule, Project Information, plans, street closure notifications -
<https://www.wirapids.org/construction-projects.html>
