


WISCONSIN RAPIDS PUBLIC WORKS DIVISION
PUBLIC WORKS PROJECT UPDATES
April 13th, 2021 Update #2

Director of Public Works:

Joseph Terry
Phone (715)-421-8255
Email JTerry@wirapids.org

City Engineer:

Joe Eichsteadt
Phone (715)-421-8251
Email Jeichsteadt@wirapids.org

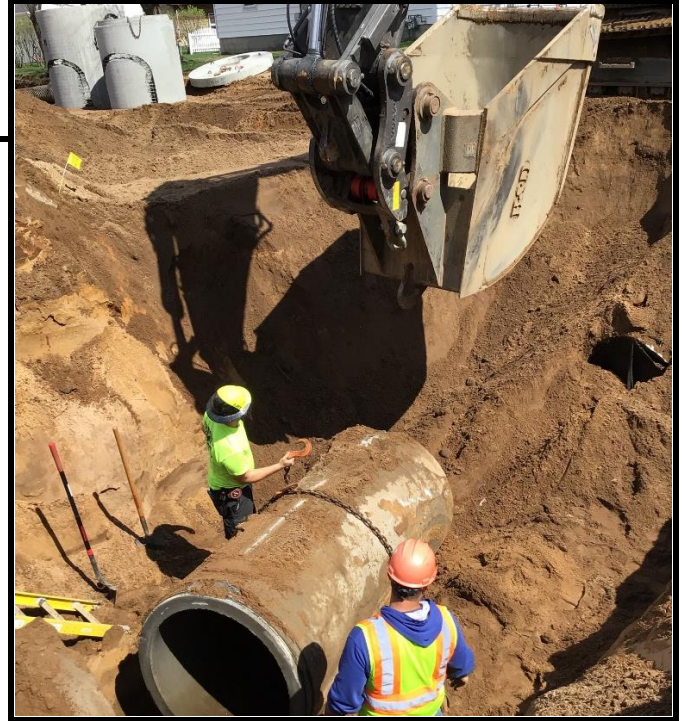

15th St N Storm Sewer

- **15th St N (Apricot St to Norton St)**
 - This week city crews are installing storm sewer structures and storm sewer piping between Apricot St and Irving St.
 - Following storm sewer installation, city crews will be working on water main and water services between Apricot St and Irving St.
- **Jefferson St (25th Ave N to east terminus)**
 - Anticipated to begin late April / early May.
- **Grove Ave Utility Extension (Quadplex Project)**
 - Sewer and water service installation began on March 24th and was completed on March 29th.
 - Main line utilities will be installed on Grove Ave from 21st PI S approximately 500' west. Work is scheduled for later in the summer.

For more information please follow these links

Construction Schedule - <https://tinyurl.com/3792acfb>

Project Information, plans, street closure notifications - <https://www.wirapids.org/construction-projects.html>
