

WISCONSIN RAPIDS PUBLIC WORKS DIVISION
PUBLIC WORKS PROJECT UPDATES
May 3rd, 2024 Update #5

City Engineer:

Joe Eichsteadt, PE
Phone (715) 421-8251
Jeichsteadt@wirapids.org

Assistant City Engineer:

Nick Dums, PE
Phone (715) 421-8209
Ndums@wirapids.org

Public Works Superintendent

Paul Vollert
Phone (715) 421-8218
Pvollert@wirapids.org



Lincoln Street near Witter Street

○ **Lincoln Street (Expressway to E Grand Ave)**

Current Phase: Phase 2 – (4/18/24 to 5/15/24)

Current Closure: Intersection at Chestnut St and north along Lincoln St thru Witter Street. The closure extends thru Witter St to a point approximately 500' north of Witter St. Local traffic can still enter from the north at Peach St and from the south at Chestnut St. D St property owners can still access D St from Chestnut St.

Proposed Closure: Next closure will be Phase 3 – Peach St intersection beginning May 16th.

This Week

- Water main and sanitary sewer work was completed on Lincoln St at Witter St with some utilities being installed 150' north of Witter St. Also, Solarus worked on a utility vault at Chestnut St.

Next Week

- Storm sewer work in the Witter St intersection will be completed early in the week followed by water main and sanitary sewer installation to a point 500' north of Witter St. Crews will also have road base installed within the Witter St intersection. The survey crews are expected to start staking for curb and gutter later in the week in anticipation of concrete curb installation. Solarus plans to complete the vault installation in the Chestnut St intersection.

Project Phasing Map

https://www.wirapids.org/uploads/1/0/3/3/103347874/construction_schedule_03262024.pdf


○ **Oak St cul-de-sac east of 20th St S**

Asphalt pavement will be scheduled as soon as asphalt plants are operational.

○ **Sidewalk Maintenance**

Restoration of the sidewalk maintenance was completed this week with all areas topsoiled and hydroseeded.

- **Curb Maintenance**
Restoration activities are expected to begin next week.

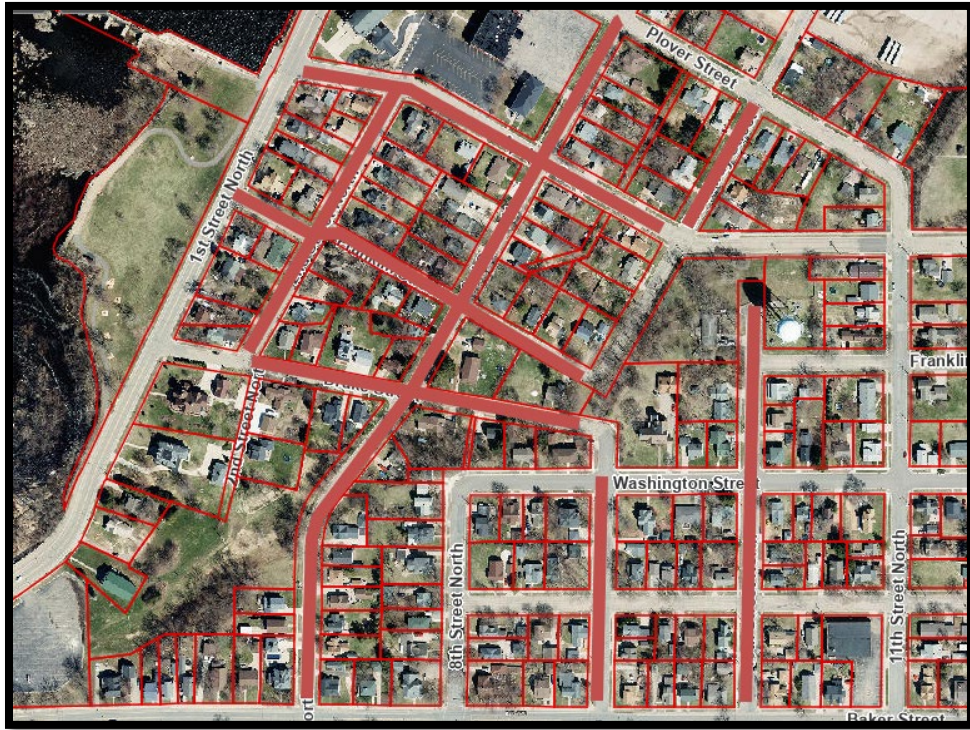

2024 Curb Maintenance Area

For more information please follow these links

Project Information, plans, schedule, street closure notifications - <https://www.wirapids.org/construction-projects.html>
